

NARAYANI STUDIOS LLP

Architecture change report

Visual Design Brief v1 versus the live website.

Proof screenshots | Sitemap | Services | Remaining work | 10-day go-live plan

28 brief sections mapped 10 shipped as specified 13 shipped with architecture changed 10 days to live after assets


Prepared for the client

14 August 2026

Live captures from the staging build (localhost:3000).

The brief asked for five cream-coloured tabs and six equal services. The live site is a noir production house: Home / About / Services / Team / Work, a three-stage spine, production crafts as their own URLs, and a compiled house reel on the hero.

1. Sitemap

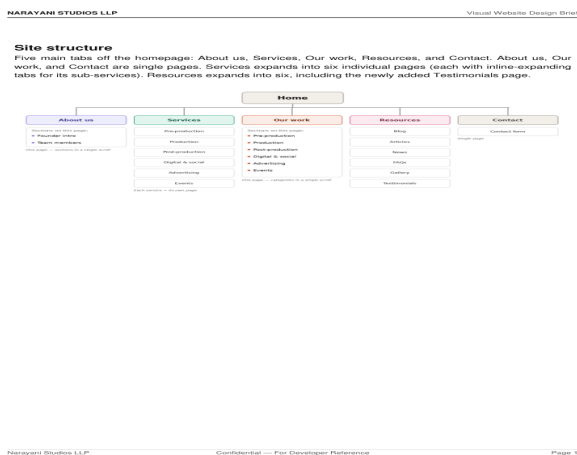

Brief: Home, About, Services (6 pages), Our work, Resources (6), Contact.


Nav

Brief: About, Services, Our work, Resources, Contact. Live: Home, About, Services, Team, Work + Enquire.

Why

Team visible in the bar; Index for the 12 business objects; Work named instead of Our work.

2. Home

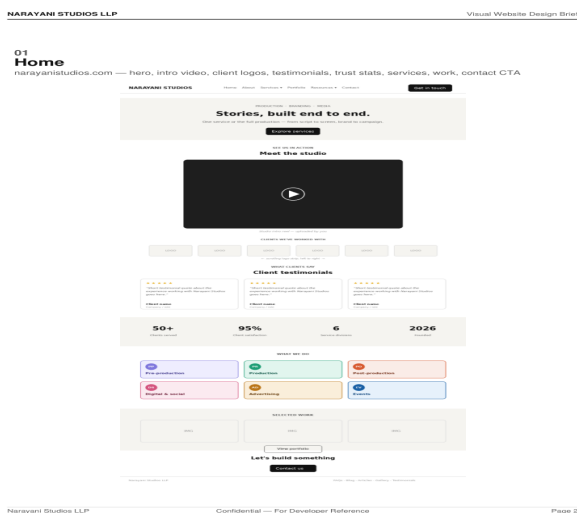

Brief cream home: Stories built end to end; intro video; logos; testimonials; 6 service cards.

Visual system

Cream mockup replaced with Obsidian Noir x Champagne after the business-objects brief.

Hero

Play-button intro video replaced by one compiled house reel.

Headline


Stories, built end to end -> Brand it. Shoot it. Finish it.

Services on home


6 equal cards -> 3 spine cards. Digital, ads, events live under /services.

Logos / stats / quotes


Not on home. No real logos or numbers from the client yet.

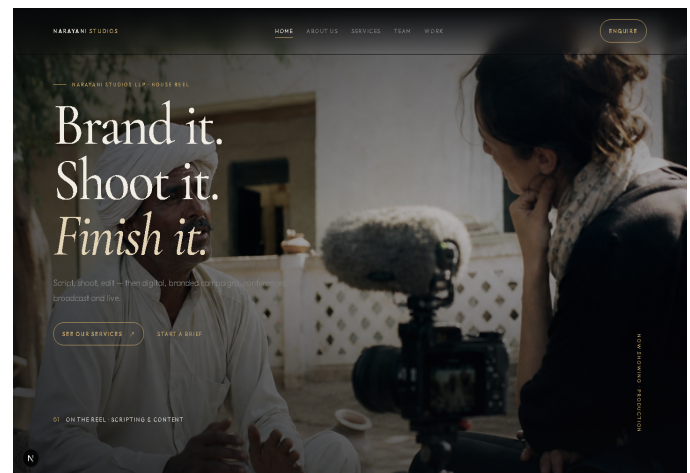


Live header: HOME, ABOUT US, SERVICES, TEAM, WORK, ENQUIRE.

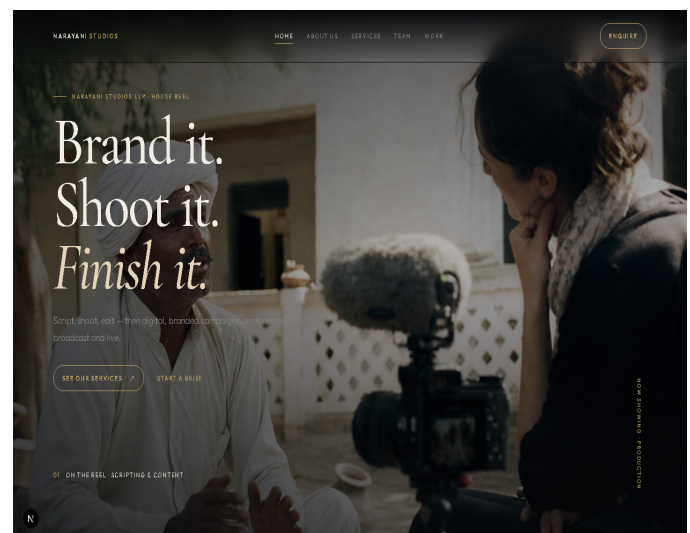

Live hero: Brand it. Shoot it. Finish it. House reel. Pre / Production / Post rail.

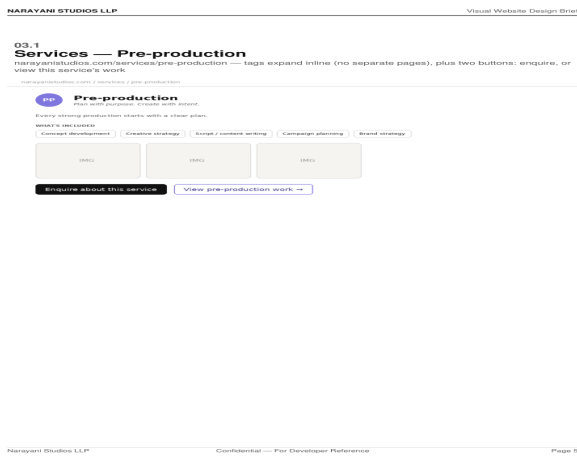

Brief Pre-production: one page, inline tags, Enquire + View this service's work.

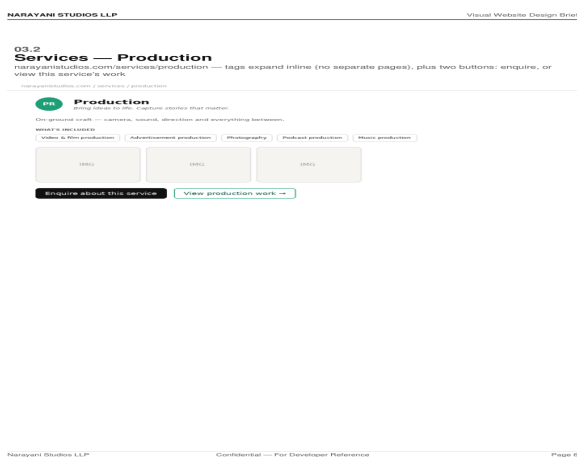

Brief Production: inline tags only, same pattern as Pre.

Routes live now:

/services Overview of all six divisions


/services/pre-production One page, tabbed crafts (matches brief)

/services/production Hub of tiles (changed from brief)


/services/production/{craft} 7 separate pages - added after you asked each craft to have its own page

/services/post-production One page, tabbed crafts (matches brief)


/services/digital-social Division pages as in the brief

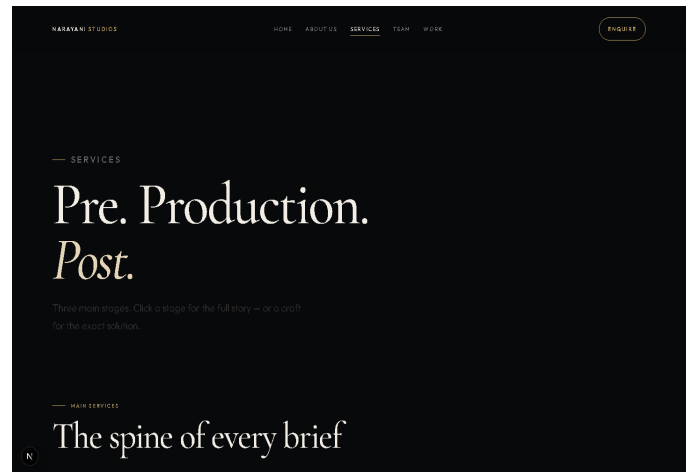


Live /services: Pre. Production. Post. then Digital, Advertising, Events.

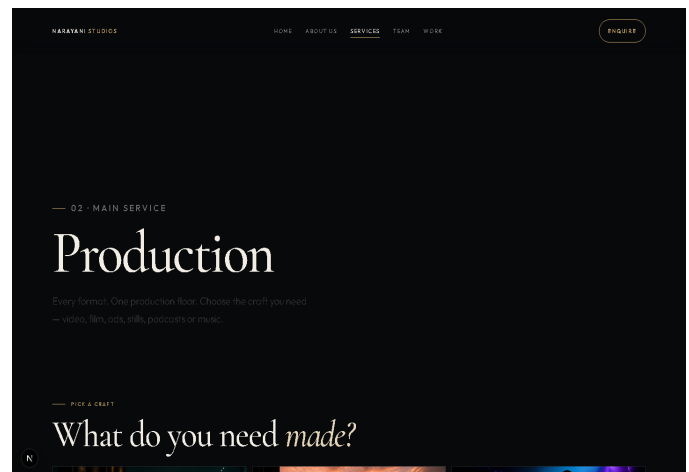

Live /services/production: each craft opens its own page.

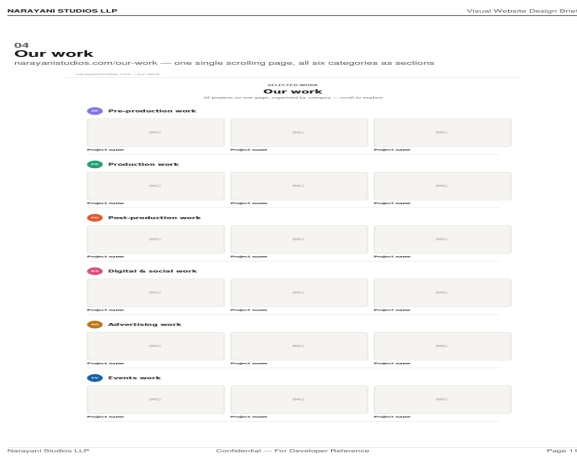

Brief: one scrolling page, six category bands, 3 project slots each (18 frames).

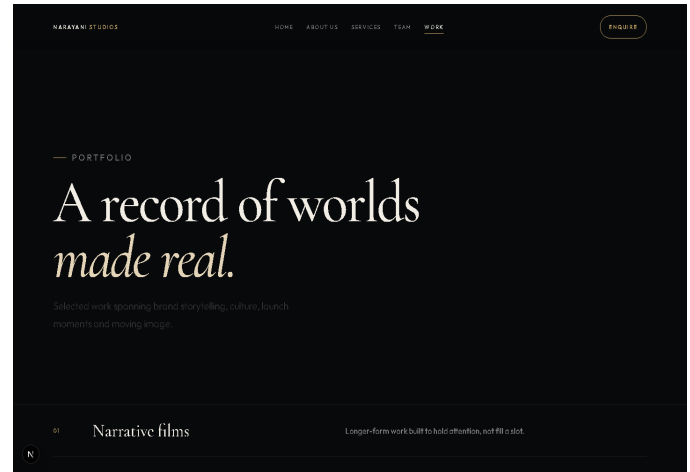

Live Work / portfolio. Structure is live; frames are placeholders until real stills arrive.

Work tab goes to /portfolio. /our-work exists but shows four placeholder frames (Northbound, Afterglow, Signal, Volume), not six category sections.

Pending work

Clock starts when the asset pack arrives. Plan is 10 working days through testing and go-live, one developer, files in one folder.

01. Swap stock house reel for client dailies (shoot, edit, campaigns, conference, broadcast, live)
02. Our work: six category sections with real projects (3+ each)
03. Client logos + trust stats + real testimonials
04. Founder / team photos and bios
05. Blog, articles, news, gallery from real studio files
06. Per-service view-this-work galleries + Enquire destinations
07. Lock nav to five PDF tabs if the client prefers the brief over the current IA
08. Contact: phone, address, GST, WhatsApp, social URLs
09. Device and browser testing, form checks, video fallbacks
10. Production build, deploy, live smoke test

House reel / process clips

MP4, 1080p, 8-20 sec each. Shooting, editing, scripting, digital, branded campaign, conference, broadcast, live show

Work stills

JPG/PNG, landscape. 3 projects x 6 categories = 18 frames + titles + year

Client logos

SVG or PNG on transparent. 6-12 marks they approve

Trust numbers

Text. Clients served, years, satisfaction - only if they will stand behind them

Testimonials

Text + name + company. 3-6 real quotes, written permission

Founders / team

Portrait photos + 40-word bio. Shreeraj, Kiran, plus any department heads

Contact

Text. Email, phone, city, GSTIN, Instagram / LinkedIn

Resources

Docs or Google Drive. 2-4 posts, 4-8 gallery stills from set

Legal

PDF or text. Privacy / terms if they want those pages

10-day plan - content, test, deploy

Day 1 starts the morning after the full pack is in one folder. Late files push deploy past day 10. Testing and go-live are days 8-10.

- | | |
|---------------|--|
| Day 1 | Ingest Drive pack. Contact, GST, social, Enquire inbox. |
| Day 2 | Founder and team photos, bios. Logos and trust numbers on home. |
| Day 3 | Testimonials. Our work: Pre, Production, Post sections. |
| Day 4 | Our work: Digital, Advertising, Events. Titles and years. |
| Day 5 | Per-service work links. Optional five-tab nav lock. |
| Day 6 | Recut house reel from shooting, edit, campaign, conference, broadcast, live clips. |
| Day 7 | Blog, news, gallery, resources copy. Legal pages if sent. |
| Day 8 | QA: Chrome, Edge, Safari, phone, tablet. Forms, 404s, video autoplay. |
| Day 9 | Fix bugs from QA. Client preview on staging. One revision pass. |
| Day 10 | Production build, deploy, live smoke test, handover. |

Clock rule: Day 1 starts the morning after the full pack is in one folder. Late files push deploy past day 10.
